Status Report #1: Procure-to-Ship

Hearth & Desk Supply Co. | Odoo 20 | Mid-project report

Report date	Period	Prepared by	Overall status
Fri 10/16/2026	10/8 to 10/16	Sawandi Kirby, project lead	Amber

Summary

Seven of ten milestones are done. Greenline Bamboo Supply missed its 10/14 delivery, sent a partial on 10/15 and shipped the remaining 24 panels and 24 shelf boards today, so M6 closed two days late. The partial covered every open manufacturing order, which kept M7 on its baseline and left all nine customer orders on track for their 10/19 promise date. Shipping starts Saturday 10/17.

Status is Amber because of the M6 slip. The issue is closed and nothing downstream moved.


Status by Area

Area	Status	Notes
Schedule	Amber	M6 (Greenline received in full) finished 10/16 against a 10/14 baseline, +2 days. M1-M5 and M7 on baseline.
Supply	Green	All 5 POs received. Greenline was the single-source risk (R2); it became issue I2 and closed today.
Manufacturing	Green	All 7 manufacturing orders produced. One posting error on 10/13 was corrected the same day (I1).
Customer orders	Green	9 sales orders confirmed across 2 waves, all promised 10/19. Finished-goods stock covers every order.

Milestones: Baseline vs Actual

Milestones: Baseline vs Actual

ID	Milestone	Owner	Baseline	Forecast	Actual	Variance (days)	Status
M1	Customers + wave 1 SOs entered, POs confirmed to all 5 vendors	Sales / Purchasing	10/9/2026		10/9/2026	0	Done
M2	Fastline + Packwell received, bills posted	Purchasing / AP	10/10/2026		10/10/2026	0	Done
M3	Ironcrest received + bill, Cable Tray MO produced	Purchasing / Manufacturing	10/12/2026		10/12/2026	0	Done
M4	Wave 2 SOs (4) confirmed	Sales	10/12/2026		10/12/2026	0	Done
M5	Brightform received, Laptop Riser MO produced, Replenishment rerun	Purchasing / Manufacturing	10/13/2026		10/13/2026	0	Done
M6	Greenline received in full	Purchasing	10/14/2026	10/16/2026	10/16/2026	2	Done
M7	Remaining MOs complete (Desk Organizer, Monitor Stand)	Manufacturing	10/15/2026		10/15/2026	0	Done
M8	All SOs shipped, carrier assignment done	Shipping	10/19/2026				Not started
M9	Vendor bills paid, exports + KPI dashboard	AP / Analytics	10/20/2026				Not started
M10	Repo pushed, Odoo database deleted	Project lead	10/21/2026				Not started

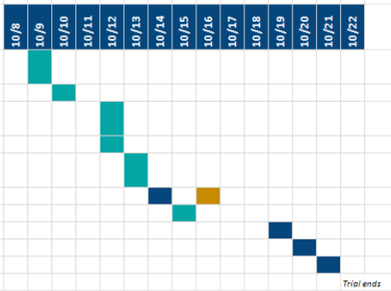

Legend

- Baseline date
- Actual, on time or early
- Actual late, or forecast slip

Variance uses Actual when filled, otherwise Forecast. Positive = days late.

KPIs

KPI	Value	How it's measured
Vendor on-time rate	80%	Receipts on or before the expected date. 4 of 5 POs; Greenline was the miss.
Vendor fill rate	98.2%	Qty on first receipt / qty ordered. Greenline's partial delivered 98 of 146 units.
Schedule variance	0.29 days	Average milestone variance, positive = late. Only M6 is off baseline.
Customer OTIF	After M8	Measured once orders ship 10/17-10/19.
Order cycle time	After M8	Ship date minus confirm date, averaged over shipped orders.

Issues and Corrections

ID	What happened	Fix	Lesson
I1 10/13	WH/MO/00004 (Laptop Riser x22) consumed its components but recorded 0 finished units, and Odoo cancelled the MO.	Inventory adjustment returned the components with a reversal reference. Replacement WH/MO/00005 produced 22 the same morning.	Produce MOs with the form's Produce button and check the finished qty before marking done.
I2 10/14	Greenline missed its 10/14 date. Partial 10/15: 50 of 74 panels, 48 of 72 shelf boards.	Received the partial, created backorder WH/IN/00006, received it in full 10/16.	A single-source vendor with the longest lead time needs a partial-shipment plan before the due date.
Correction 10/15	WH/MO/00002 (Monitor Stand) was rescheduled to 10/16 before checking stock. The partial had already covered it.	Date reverted and the wrong note removed. The chatter keeps the round trip. MO produced 10/15.	Check component availability after a receipt before rescheduling anything.

Next 5 Days

- Sat 10/17 to Mon 10/19 (M8): ship all 9 sales orders, assign carriers. Coastal Express covers FL, GA, NC and SC only (A2).
- Tue 10/20 (M9): pay the Fastline and Packwell bills, then export data and build the KPI dashboard.
- Wed 10/21 (M10): push the repo, delete the Odoo database.
- Watch item R1: the trial ends 10/22. Exports on 10/20 leave a two-day buffer.

Note: Hearth & Desk Supply Co. is a fictional company run inside a real Odoo 20 trial. The vendor disruptions were designed scenarios, and vendor lead times were compressed so every receipt landed inside the trial (A1). The transactions, errors and corrections above all happened in the system.
